

CompTIA

Exam Questions PK0-005

CompTIA Project+ Certification Exam



NEW QUESTION 1

DRAG DROP -

During a gate review meeting, the deliverable was rejected by the customer.

Review the dashboard.

Part 1: Drag and drop each task, placing them in the correct order based on the project change control process.

Part 2: Select the proper document(s) to be updated.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

 Dashboard

Drag and Drop

Perform a demonstration.

Define new requirements and record changes.

Update and test the deliverable.

Consult the RACI matrix.

Assess the schedule, risk, and cost.

Obtain a sign off.

Make an announcement on the company portal.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

 Dashboard

Question Options

Select the appropriate document(s) to update.

☐

 Risk register

☐

 Schedule

☐

 Statement of work

☐

 Organizational chart

☐

 Change log

☐

 Issues log

☐

 WBS dictionary

- A. Mastered
- B. Not Mastered

Answer: A

Explanation:

Part 1
Part 2

Change Control Process

1

Define new requirements and record changes.

2

Assess the schedule, risk, and cost.

3

Update and test the deliverable.

4

Perform a demonstration.

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

Dashboard

Drag and Drop

Perform a demonstration.

Define new requirements and record changes.

Update and test the deliverable.

Consult the RACI matrix.

Assess the schedule, risk, and cost.

Obtain a sign off.

Make an announcement on the company portal.

Part 1
Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

☒ Statement of work

7

☒ Schedule

8

☒ Change log

Dashboard

Question Options

Select the appropriate document(s) to update.

☐ Risk register

☐ Schedule

☐ Statement of work

☐ Organizational chart

☐ Change log

☐ Issues log

☐ WBS dictionary

NEW QUESTION 2

Following a successful release, a project manager sent a survey to all stakeholders to gain an understanding of opportunity areas for the team. Which of the following can use the survey results as an input?

- A. Daily stand-up
- B. Project momentum
- C. Performance feedback
- D. Meeting minutes

Answer: B

NEW QUESTION 3

Which of the following BEST describes how an organization should coordinate management of multiple related projects?

- A. Apply the SDLC process.
- B. Establish a program.
- C. Consult the CCB.
- D. Use different frameworks.

Answer: B

NEW QUESTION 4

A project team gathers weekly to review its progress. Which of the following is the project manager MOST likely to have prepared to ensure team members who are absent remain informed about assignments?

- A. Status report
- B. Project plan
- C. Change log
- D. Meeting minutes

Answer: D

NEW QUESTION 5

A project manager realizes that a project will not be completed on time due to resource constraints. Which of the following actions should the project manager take NEXT?

- A. Trigger the contingency plan and communicate with the stakeholders.

- B. Work with the functional managers to create a work-around.
- C. Submit a change request to the change control board.
- D. Transfer the risk by hiring a new vendor who was successful on a previous project.
- E. Set up an escalation meeting with the sponsor.

Answer: A

NEW QUESTION 6

Which of the following should occur when implementing an IT infrastructure change that takes risks into consideration?

- A. Approving the change request
- B. Developing a rollback plan
- C. Gathering necessary resources
- D. Defining requirements

Answer: B

NEW QUESTION 7

The project team determines that software installation can only begin after the desktops have been installed and can be powered on. Which of the following dependencies does this represent?

- A. External
- B. Internal
- C. Mandatory
- D. Discretionary

Answer: B

NEW QUESTION 8

A third party needs to perform a short-term task for which the duration cannot be accurately estimated and the cost cannot be calculated in advance. Which of the following should the project manager put in place before work begins?

- A. Time and materials contract
- B. Master service agreement
- C. Fixed-price contract
- D. Statement of work
- E. Cost-plus agreement

Answer: A

NEW QUESTION 9

Which of the following would be MOST beneficial to do before a call to ensure all meeting items are addressed and the correct participants attend?

- A. Assign action items to attendees.
- B. Distribute an agenda
- C. Most Voted
- D. Email the minutes from the previous meeting.
- E. Schedule a convenient time.

Answer: B

NEW QUESTION 10

Which of the following is a quality assurance tool?

- A. Defining project goals
- B. Identifying the root cause analysis
- C. Assessing employee efficiency
- D. Assessing skill gaps

Answer: D

NEW QUESTION 10

Due to multiple changes, the sign-off for the project scope baseline is delayed. The project sponsor has restricted the budget for this project. Which of the following should the project manager MOST likely do to move forward?

- A. Communicate with the affected stakeholders.
- B. Initiate a formal change request to modify the cost.
- C. Adjust the scope to stay within the cost.
- D. Set a new cost using a lightweight estimation method.

Answer: C

NEW QUESTION 15

An opportunity emerged in the middle of a project life cycle. Which of the following is the BEST action for the project manager to take?

- A. Exploit the risk.
- B. Accept the risk.
- C. Avoid the risk.
- D. Transfer the risk.

Answer: D

NEW QUESTION 17

A project manager was just assigned to a new project. Which of the following activities should the project manager undertake after accepting the project? (Choose two.)

- A. Review the detailed plan.
- B. Develop a preliminary scope.
- C. Develop a transition plan.
- D. Develop a project management plan.
- E. Review the resource pool.
- F. Review the project objectives.

Answer: AF

NEW QUESTION 20

Halfway through a project, the sponsor states that the project is taking too long to complete. Which of the following should the project manager consult?

- A. Gantt chart
- B. Maintenance window schedule
- C. Functional requirements
- D. Test results

Answer: A

NEW QUESTION 21

A project manager is assigned to a multinational project with team members from different continents. Which of the following is the MOST important aspect for the project manager to consider?

- A. Resource allocation
- B. Communication security
- C. Technological factors
- D. Cultural differences

Answer: D

NEW QUESTION 25

After determining the appropriate maintenance window, which of the following should occur NEXT in the operational infrastructure change process?

- A. Implement the change.
- B. Approve the test plan.
- C. Notify customers.
- D. Develop a rollback plan.

Answer: B

NEW QUESTION 29


Which of the following offers administrators more direct control over operating systems?

- A. Infrastructure as a service
- B. Software as a service
- C. Functions as a service
- D. Platform as a service

Answer: D

NEW QUESTION 31

A project sponsor asked the PM to provide a summary of the current financial status. The PM uses the following burn up chart for the analysis:

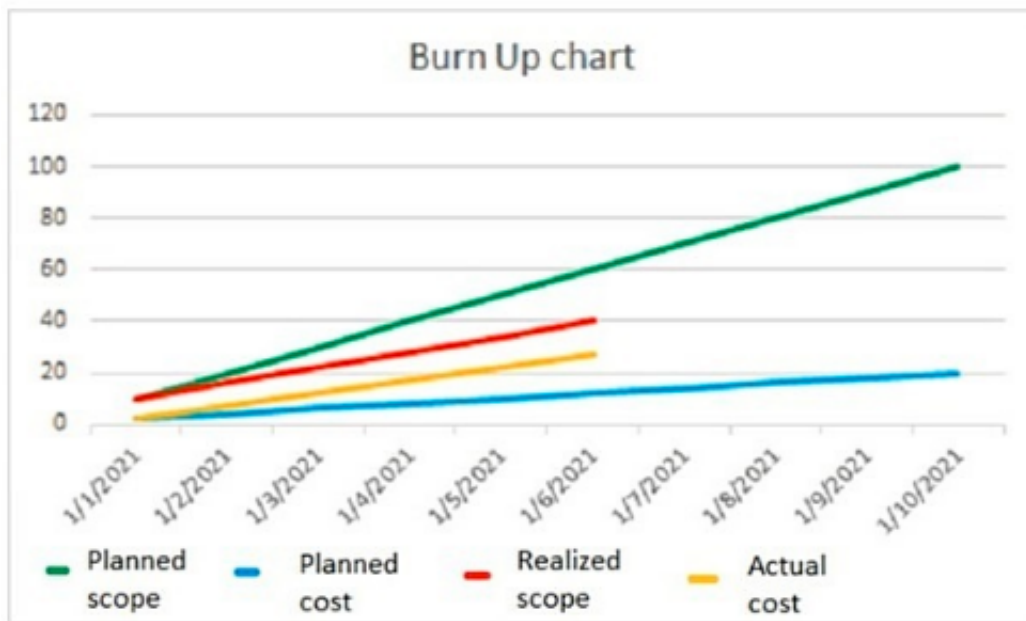

Based on the chart, which of the following is the current status of the project?

- A. Behind schedule and over budget
- B. Behind schedule and under budget
- C. Ahead of schedule and over budget
- D. Ahead of schedule and under budget

Answer: B

NEW QUESTION 32

.....

Thank You for Trying Our Product

We offer two products:

1st - We have Practice Tests Software with Actual Exam Questions

2nd - Questions and Answers in PDF Format

PK0-005 Practice Exam Features:

- * PK0-005 Questions and Answers Updated Frequently
- * PK0-005 Practice Questions Verified by Expert Senior Certified Staff
- * PK0-005 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- * PK0-005 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year

100% Actual & Verified — Instant Download, Please Click
[Order The PK0-005 Practice Test Here](#)
